

Heads Up



WHERE & WHEN:

Waikaremoana, G4 Turbine Pit, 19th June 2018

WHAT HAPPENED?

The Turbine bearing was being removed when one of the lever hoists disengaged under load. A secondary lever hoist was in place, so the load didn't drop far. All the lever hoists used were under current test and tag.

WHAT COULD HAVE HAPPENED?


If there had been no secondary hoist attached, the load would have fallen into the pit causing damage and potential injury.

WHAT ARE WE DOING?

Investigating to check for the reason for the failure.

YOUR INPUT & ACTION REQUIRED

- This Safety Alert is a reminder that equipment can fail unexpectedly.
- Remember, where ever possible, to ensure secondary levels of protection are in place to prevent failure.
- Ask yourself as you plan and prepare for your work "What extra measures can be put into place to make sure that even when things go wrong, they go right?"

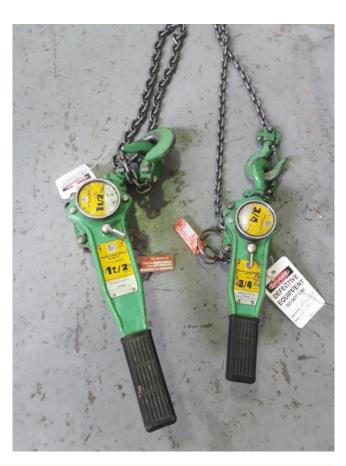

THANKS FOR YOUR COMMITMENT TO A SAFER WORKPLACE
